


Project1-Update 12-17-18.mpp

	Task Name	Duration	Start	Finish
1	2018 Curb Ramp and Sidewalk Repair Program	107 days	Mon 10/1/18 8:00 AM	Mon 3/11/19 5:00 PM
2	Submittal Review	30 days	Mon 10/1/18 8:00 AM	Fri 11/9/18 5:00 PM
3	NTP	0 days	Fri 11/9/18 5:00 PM	Fri 11/9/18 5:00 PM
4	Begin Construction	77 days	Tue 11/13/18 8:00 AM	Mon 3/11/19 5:00 PM
5	Mobilize/Set up Yard	2 days	Tue 11/13/18 8:00 AM	Wed 11/14/18 5:00 PM
6	Sidewalk Repairs	75 days	Thu 11/15/18 8:00 AM	Mon 3/11/19 5:00 PM
7	Group#1	5 days	Thu 11/15/18 8:00 AM	Wed 11/21/18 5:00 PM
8	1600 Kearney St	5 days	Thu 11/15/18 8:00 AM	Wed 11/21/18 5:00 PM
9	6523 Potrero Ave	5 days	Thu 11/15/18 8:00 AM	Wed 11/21/18 5:00 PM
10	7141 Potrero Ave	5 days	Thu 11/15/18 8:00 AM	Wed 11/21/18 5:00 PM
11	7806 Potrero Ave	5 days	Thu 11/15/18 8:00 AM	Wed 11/21/18 5:00 PM
12	Group #2	5 days	Tue 12/4/18 8:00 AM	Mon 12/10/18 5:00 PM
13	707 Moeser lane	2 days	Tue 12/4/18 8:00 AM	Wed 12/5/18 5:00 PM
14	1520 Douglas Dr	5 days	Tue 12/4/18 8:00 AM	Mon 12/10/18 5:00 PM
15	500 Kearney St	5 days	Tue 12/4/18 8:00 AM	Mon 12/10/18 5:00 PM
16	6630 Cutting Blvd	5 days	Tue 12/4/18 8:00 AM	Mon 12/10/18 5:00 PM
17	8509 Roberta Dr	2 days	Tue 12/4/18 8:00 AM	Wed 12/5/18 5:00 PM
18	Group #3	11 days	Tue 12/18/18 8:00 AM	Mon 1/7/19 5:00 PM
19	2303 Edith ST	1 day	Tue 12/18/18 8:00 AM	Tue 12/18/18 5:00 PM
20	1345 Elm ST	2 days	Thu 12/27/18 8:00 AM	Fri 12/28/18 5:00 PM
21	907 Richmond ST	2 days	Wed 1/2/19 8:00 AM	Thu 1/3/19 5:00 PM
22	1237 Richmond St	2 days	Fri 1/4/19 8:00 AM	Mon 1/7/19 5:00 PM
23	7320 Plank Ct	1 day	Fri 1/4/19 8:00 AM	Fri 1/4/19 5:00 PM
24	Group #4	43 days	Tue 1/8/19 8:00 AM	Mon 3/11/19 5:00 PM
25	6814 Fairmount Ave	2 days	Tue 1/8/19 8:00 AM	Wed 1/9/19 5:00 PM
26	6818 Fairmount Ave	3 days	Tue 1/8/19 8:00 AM	Thu 1/10/19 5:00 PM
27	332 Coronado ST	2 days	Wed 1/16/19 8:00 AM	Thu 1/17/19 5:00 PM
28	Curb Ramp Repairs	40 days	Fri 1/11/19 8:00 AM	Mon 3/11/19 5:00 PM
29	COR#1-Additional Ramps at Gladys Sea	5 days	Fri 1/11/19 8:00 AM	Thu 1/17/19 5:00 PM
30	HAgan-Mira Vista-CANYon Trail 4ea	4 days	Wed 1/16/19 8:00 AM	Tue 1/22/19 5:00 PM
31	3213 Santa Clara Ave	2 days	Wed 1/23/19 8:00 AM	Thu 1/24/19 5:00 PM
32	3225 Santa Clara Ave	2 days	Wed 1/23/19 8:00 AM	Thu 1/24/19 5:00 PM
33	Central & Santa Clara 2ea	4 days	Fri 1/25/19 8:00 AM	Wed 1/30/19 5:00 PM
34	5806 Central	2 days	Thu 1/31/19 8:00 AM	Fri 2/1/19 5:00 PM
35	5813 Central Ave	2 days	Thu 1/31/19 8:00 AM	Fri 2/1/19 5:00 PM
36	5914 Central Ave	2 days	Thu 1/31/19 8:00 AM	Fri 2/1/19 5:00 PM
37	Carlson & Central 4ea	5 days	Mon 2/4/19 8:00 AM	Fri 2/8/19 5:00 PM
38	3020 Carlson	2 days	Mon 2/11/19 8:00 AM	Tue 2/12/19 5:00 PM
39	3201 Carlson	2 days	Mon 2/11/19 8:00 AM	Tue 2/12/19 5:00 PM
40	Carlson San Diego 2ea	4 days	Wed 2/13/19 8:00 AM	Tue 2/19/19 5:00 PM
41	CARlson & AVila 4ea	4 days	Wed 2/20/19 8:00 AM	Mon 2/25/19 5:00 PM
42	Carlson & EL Dorado 4ea	4 days	Tue 2/26/19 8:00 AM	Fri 3/1/19 5:00 PM
43	Central & Yosemite 4ea	4 days	Mon 3/4/19 8:00 AM	Thu 3/7/19 5:00 PM
44	1021 Richmond ST	2 days	Fri 3/8/19 8:00 AM	Mon 3/11/19 5:00 PM
45	Punch List & Close Out	2 days	Mon 3/4/19 8:00 AM	Tue 3/5/19 5:00 PM

Critical		Baseline Milestone	
Critical Split		Milestone	
Critical Progress		Summary Progress	
Task		Summary	
Split		Manual Summary	
Task Progress		Project Summary	
Manual Task		External Tasks	
Start-only		External Milestone	
Finish-only		Inactive Task	
Duration-only		Inactive Milestone	
Baseline		Inactive Summary	
Baseline Split		Deadline	

Project1-Update 12-17-18.mpp

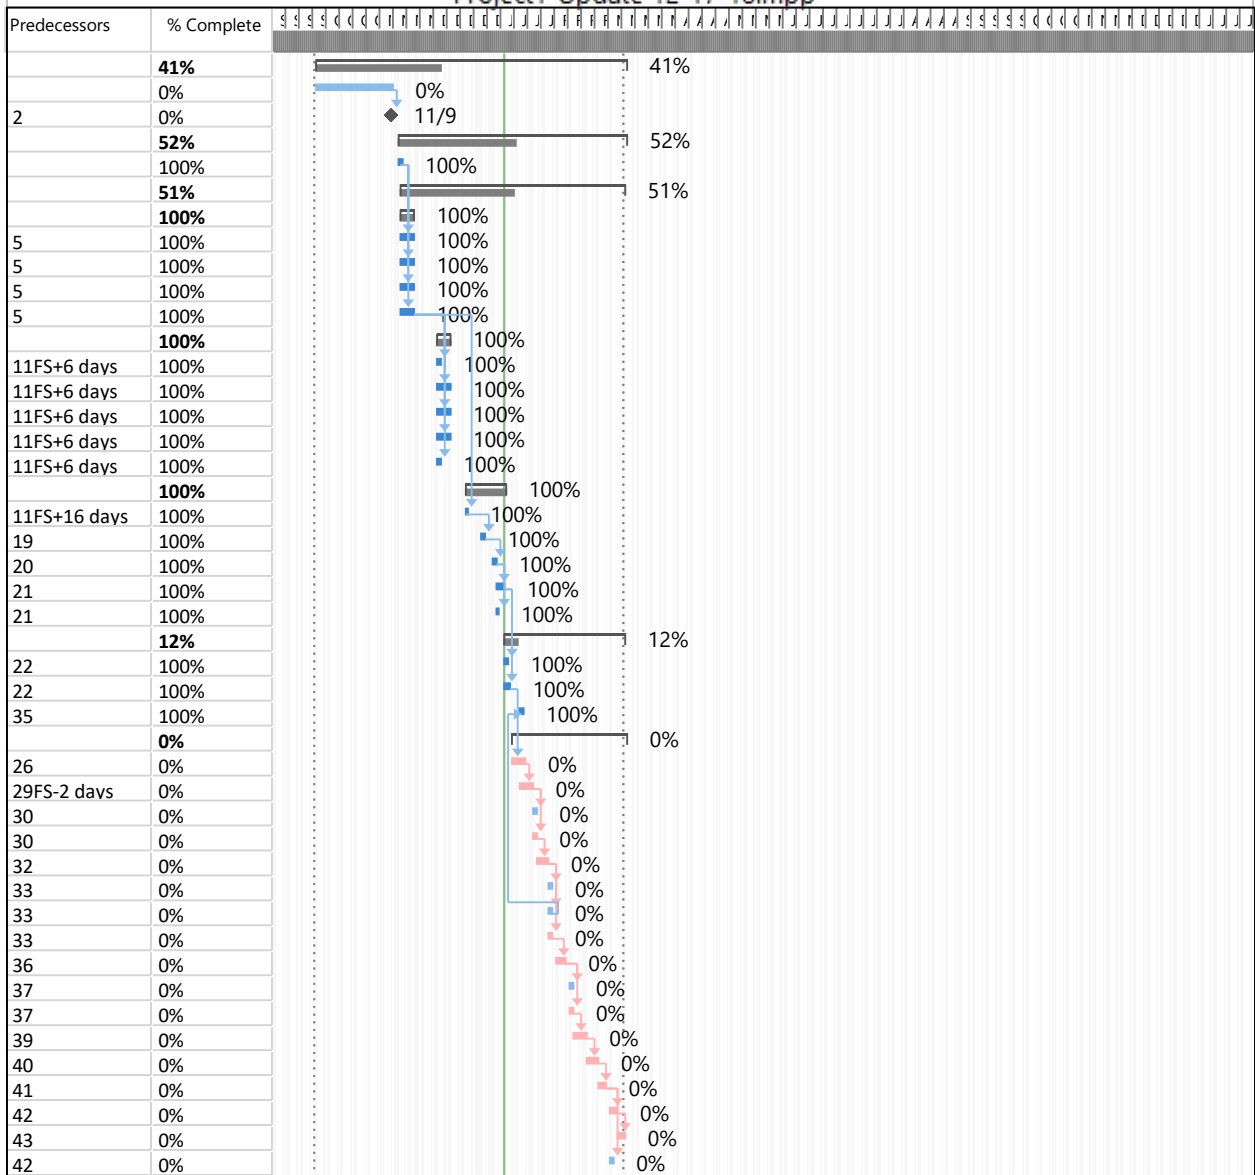

Critical		Baseline Milestone	
Critical Split		Milestone	
Critical Progress		Summary Progress	
Task		Summary	
Split		Manual Summary	
Task Progress		Project Summary	
Manual Task		External Tasks	
Start-only		External Milestone	
Finish-only		Inactive Task	
Duration-only		Inactive Milestone	
Baseline		Inactive Summary	
Baseline Split		Deadline	
